


CONTACT	PHONE	DATE
PROJECT NAME		
CUSTOMER	EMAIL	
LOCATION	DESIRED DELIVERY DATE	

// PRODUCT

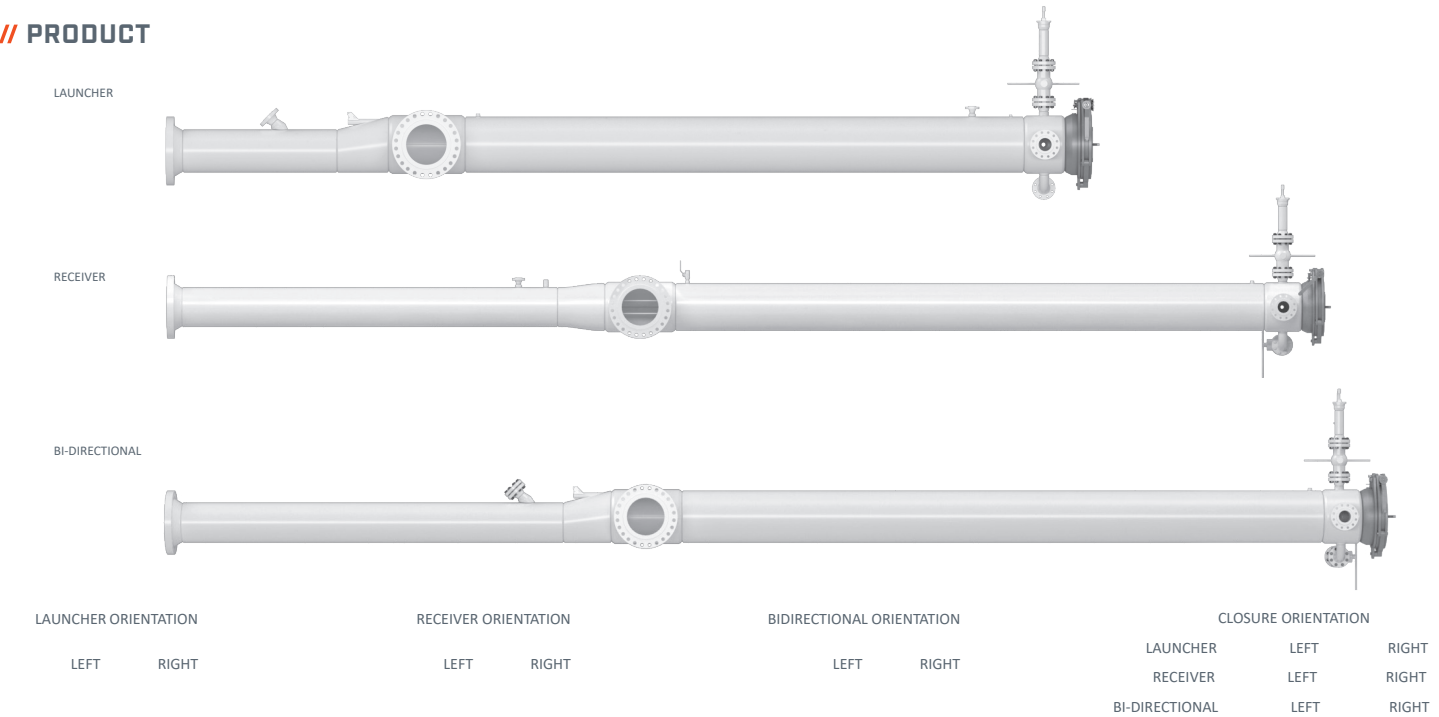

// SPECIFICATIONS

OUTSIDE DIAMETER - NOMINAL PIPE	IN.	MM.
WALL THICKNESS - NOMINAL PIPE	IN.	MM.
YIELD STRENGTH - NOMINAL PIPE		
DESIGN CODE	B31.3	B31.4 B31.8 OTHER
DESIGN FACTOR	0.72	0.60 0.50 0.40
FLANGE RATING	150	300 600 OTHER
DESIGN PRESSURE	PSI	BAR OTHER
DESIGN TEMPERAURE	MAX	F / C
	MIN	F / C
CORROSION ALLOWANCE	YES NO	IN. MM. IF YES, LIST CA HERE:
NACE MR0175 REQUIRED?	YES NO	IF YES, WELDFIT WILL ENSURE THE USE OF NACE-COMPLIANT MATERIALS NOTED ON MATERIAL TEST REPORTS (MTRS), WELD PROCEDURES THAT MEET NACE MR0175 STANDARDS, AND HARDNESS VALUES ON EXTRUSION BANDS (IF APPLICABLE) THAT COMPLY WITH NACE MR0175 REQUIREMENTS.
ADDITIONAL SOUR SERVICE REQUIREMENTS?	YES NO	IF YES, LIST HERE:
PAINT/COATING REQUIREMENTS	PRIMER ONLY	2 COATS 3 COATS OTHER *PROVIDE SPECS
TYPE OF PIGS/SCRAPERS TO LAUNCH		
NUMBER OF PIGS IN CYCLE (Launcher)	STANDARD 7(2D) pigs	EXTENDED LENGTH 10(2D) pigs up to 20 inch OTHER
NUMBER OF PIGS IN CYCLE (Reciever)	STANDARD 8(2D) pigs	EXTENDED LENGTH 11(2D) pigs up to 20 inch OTHER
TYPE OF CLOSURE NEEDED		
HYDRO TESTING REQUIRED	YES NO	4hrs 8hrs Other

// OPTIONS

SKID MOUNTED	FLOW-THROUGH PIPING	TAIL PIPING	KICKER / BY-PASS PIPING
VALVE PACKAGE	FLOW-THROUGH SKID	TAIL PIPING SKID	

ONSITE REMOTE MONITORING & CONTROL
YES NO

OPTIONAL SOLAR PANEL
YES NO

PLC

PIG SIGNALER
YES NO

MAINLINE VALVE
YES NO

OPTIONAL PIG RECEIVING TRAY
* ON RECEIVER ONLY
YES NO

EQUALIZATION VALVE

EQUALIZATION LINE

KICKER/BYPASS VALVE
YES NO

KICKER/BYPASS PIPING
YES NO

FLOW-THROUGH VALVE
YES NO

FLOW-THROUGH PIPING
YES NO

FLOW-THROUGH SKID
YES NO

TAIL PIPING
IF YES, DO YOU NEED
YES NO

TAIL PIPING SKID
YES NO

STATION BYPASS VALVE
YES NO

END VIEW

BLOW DOWN VALVE
YES NO

DRAIN VALVE
YES NO

// NOTES
